

FORM R405-2017

# FLORIDA ENERGY EFFICIENCY CODE FOR BUILDING CONSTRUCTION

Florida Department of Business and Professional Regulation - Residential Performance Method

Project Name: Sandbar Lot 1091  
Street: 4572 Arboretum CIR, Unit:BLDG 9  
City, State, Zip: , FL ,  
Owner: Mattamy Naples LLC  
Design Location: FL, NAPLES\_MUNICIPAL

Builder Name:  
Permit Office:  
Permit Number:  
Jurisdiction:  
County: Collier (Florida Climate Zone 1 )

1. New construction or existing	New (From Plans)
2. Single family or multiple family	Multi-family
3. Number of units, if multiple family	1
4. Number of Bedrooms	3
5. Is this a worst case?	No
6. Conditioned floor area above grade (ft²)	1834
Conditioned floor area below grade (ft²)	0
7. Windows(219.1 sqft.)	Description Area
a. U-Factor:	Dbl, U=0.33 219.06 ft²
SHGC:	SHGC=0.23
b. U-Factor:	N/A ft²
SHGC:	
c. U-Factor:	N/A ft²
SHGC:	
d. U-Factor:	N/A ft²
SHGC:	
Area Weighted Average Overhang Depth:	7.622 ft.
Area Weighted Average SHGC:	0.230
8. Floor Types (1834.0 sqft.)	Insulation Area
a. Slab-On-Grade Edge Insulation	R=0.0 1210.00 ft²
b. Floor Over Other Space	R=0.0 440.00 ft²
c. other (see details)	R= 184.00 ft²

9. Wall Types (2184.1 sqft.)	Insulation Area
a. Concrete Block - Int Insul, Exterior	R=4.1 1333.30 ft²
b. Concrete Block - Int Insul, Common	R=4.1 294.00 ft²
c. Frame - Wood, Exterior	R=13.0 288.00 ft²
d. other (see details)	R= 268.75 ft²
10. Ceiling Types (1567.0 sqft.)	Insulation Area
a. Under Attic (Vented)	R=30.0 1367.00 ft²
b. Knee Wall (Vented)	R=30.0 200.00 ft²
c. N/A	R= ft²
11. Ducts	R ft²
a. Sup: Attic, Ret: Attic, AH: 2nd Floor	8 361.4
12. Cooling systems	kBtu/hr Efficiency
a. Central Unit	34.8 SEER:15.00
13. Heating systems	kBtu/hr Efficiency
a. Electric Heat Pump	34.6 HSPF:8.50
14. Hot water systems	
a. Electric	Cap: 50 gallons
	EF: 0.950
b. Conservation features	
None	
15. Credits	CF, Pstat

Glass/Floor Area: 0.119  
Total Proposed Modified Loads: 57.34  
Total Baseline Loads: 64.19

**PASS**

I hereby certify that the plans and specifications covered by this calculation are in compliance with the Florida Energy Code.

PREPARED BY: Digitally signed by David A DaSilva  
DATE: DN: c=US, o=IdenTrust ACES Unaffiliated  
Individual, cn=David A DaSilva,  
0.9.2342.19200300.100.1.1=A010980000  
00163892A5AE700001488  
Date: 2018.12.05 17:10:51 -0500

I hereby certify that this building, as shown, is in compliance with the Florida Energy Code.

OWNER/AGENT: Lillian Perrone  
DATE: 12/6/18

Review of the plans and specifications covered by this calculation indicates compliance with the Florida Energy Code. Before construction is completed this building will be inspected for compliance with Section 553.908 Florida Statutes.



BUILDING OFFICIAL: \_\_\_\_\_  
DATE: \_\_\_\_\_

- Compliance requires certification by the air handler unit manufacturer that the air handler enclosure qualifies as certified factory-sealed in accordance with R403.3.2.1.
- Compliance requires an Air Barrier and Insulation Inspection Checklist in accordance with R402.4.1.1 and this project requires an envelope leakage test report with envelope leakage no greater than 7.00 ACH50 (R402.4.1.2).

## PROJECT

Title:	Sandbar Lot 1091	Bedrooms:	3	Address Type:	Lot Information
Building Type:	User	Conditioned Area:	1834	Lot #	1091
Owner Name:	Mattamy Naples LLC	Total Stories:	2	Block/Subdivision:	ARBORETUM
# of Units:	1	Worst Case:	No	PlatBook:	
Builder Name:		Rotate Angle:	270	Street:	
Permit Office:		Cross Ventilation:		County:	Collier
Jurisdiction:		Whole House Fan:		City, State, Zip:	, FL ,
Family Type:	Multi-family				
New/Existing:	New (From Plans)				
Comment:					

## CLIMATE

✓	Design Location	TMY Site	Design Temp 97.5 %	2.5 %	Int Design Temp Winter	Summer	Heating Degree Days	Design Moisture	Daily Temp Range
	FL, NAPLES_MUNICIPAL	FL_NAPLES_MUNICIPAL	46	90	70	75	288.5	58	Medium

## BLOCKS

Number	Name	Area	Volume
1	Block1	1834	16245

## SPACES

Number	Name	Area	Volume	Kitchen	Occupants	Bedrooms	Infil ID	Finished	Cooled	Heated
1	1st Floor	1210	11253	Yes	4	1	1	Yes	Yes	Yes
2	2nd Floor	624	4992	No	0	2	1	Yes	Yes	Yes

## FLOORS

✓	#	Floor Type	Space	Perimeter	Perimeter R-Value	Area	Joist R-Value	Tile	Wood	Carpet
	1	Floor over Garage	2nd Floor	----	----	184 ft²	13	0	0	1
	2	Slab-On-Grade Edge Insulatio	1st Floor	50 ft		1210 ft²	----	0.32	0	0.68
	3	Floor Over Other Space	2nd Floor	----	----	440 ft²		0.12	0	0.88

## ROOF

✓	#	Type	Materials	Roof Area	Gable Area	Roof Color	Rad Barr	Solar Absor.	SA Tested	Emitt	Emitt Tested	Deck Insul.	Pitch (deg)
	1	Gable or shed	Flat tile/slate	1710 ft²	382 ft²	Medium	N	0.85	No	0.85	No	0	26.6

## ATTIC

✓	#	Type	Ventilation	Vent Ratio (1 in)	Area	RBS	IRCC
	1	Full attic	Vented	300	1529 ft²	N	N

# INPUT SUMMARY CHECKLIST REPORT

## CEILING

✓	#	Ceiling Type	Space	R-Value	Ins Type	Area	Framing Frac	Truss Type
✓	1	Knee Wall (Vented)	2nd Floor	30	Blown	160 ft²	0.11	Wood
✓	2	Knee Wall (Vented)	2nd Floor	30	Blown	40 ft²	0.11	Wood
✓	3	Under Attic (Vented)	1st Floor	30	Blown	753 ft²	0.11	Wood
✓	4	Under Attic (Vented)	2nd Floor	30	Blown	614 ft²	0.11	Wood

## WALLS

✓	#	Ornt	Adjacent To	Wall Type	Space	Cavity R-Value	Width Ft	In	Height Ft	In	Area	Sheathing R-Value	Framing Fraction	Solar Absor.	Below Grade%
✓	1	W=>S	Exterior	Frame - Wood	2nd Floor	13	9	6	8		76.0 ft²		0.23	0.6	0
✓	2	W=>S	Exterior	Concrete Block - Int Insul	1st Floor	4.1	8	6	9	4	79.3 ft²		0	0.6	0
✓	3	N=>W	Exterior	Frame - Wood	2nd Floor	13	22	6	8		180.0 ft²		0.23	0.6	0
✓	4	N=>W	Exterior	Concrete Block - Int Insul	1st Floor	4.1	11		9	4	102.7 ft²		0	0.6	0
✓	5	E=>N	Exterior	Frame - Wood	2nd Floor	13	4		8		32.0 ft²		0.23	0.6	0
✓	6	S=>E	Exterior	Concrete Block - Int Insul	1st Floor	4.1	18	6	9	4	172.7 ft²		0	0.6	0
✓	7	N=>W	Garage	Frame - Wood	1st Floor	13	32	3	8	4	268.8 ft²		0.23	0.6	0
✓	8	W=>S	Neighbor	Concrete Block - Int Insul	1st Floor	4.1	31	6	9	4	294.0 ft²		0	0.6	0
✓	9	E=>N	Exterior	Concrete Block - Int Insul	1st Floor	4.1	50		9	4	466.7 ft²		0	0.6	0
✓	10	E=>N	Exterior	Concrete Block - Int Insul	2nd Floor	4.1	50		8		400.0 ft²		0	0.6	0
✓	11	SE=>NE	Exterior	Concrete Block - Int Insul	1st Floor	4.1	12		9	4	112.0 ft²		0	0.6	0

## DOORS

✓	#	Ornt	Door Type	Space	Storms	U-Value	Width Ft	In	Height Ft	In	Area
✓	1	N=>W		1st Floor	None	.46	2	8	6	8	17.8 ft²

## WINDOWS

Orientation shown is the entered orientation (=>) changed to As Built (rotated 270 degrees).

✓	#	Ornt	Wall ID	Frame	Panes	NFRC	U-Factor	SHGC	Imp	Area	Overhang Depth	Separation	Int Shade	Screening
✓	1	W=>S	2	Vinyl	Low-E Double	Yes	0.33	0.23	N	48.0 ft²	11 ft 7 in	0 ft 2 in	None	None
✓	2	N=>W	3	Vinyl	Low-E Double	Yes	0.33	0.23	N	30.0 ft²	1 ft 0 in	0 ft 5 in	None	None
✓	3	N=>W	3	Vinyl	Low-E Double	Yes	0.33	0.23	N	20.0 ft²	1 ft 0 in	1 ft 8 in	None	None
✓	4	N=>W	4	Vinyl	Low-E Double	Yes	0.33	0.23	N	21.3 ft²	7 ft 4 in	0 ft 0 in	None	None
✓	5	N=>W	4	Vinyl	Low-E Double	Yes	0.33	0.23	N	11.8 ft²	7 ft 4 in	0 ft 0 in	None	None
✓	6	S=>E	6	Vinyl	Low-E Double	Yes	0.33	0.23	N	40.0 ft²	1 ft 4 in	0 ft 9 in	None	None
✓	7	S=>E	6	Vinyl	Low-E Double	Yes	0.33	0.23	N	48.0 ft²	16 ft 0 in	0 ft 2 in	None	None

## GARAGE

✓	#	Floor Area	Ceiling Area	Exposed Wall Perimeter	Avg. Wall Height	Exposed Wall Insulation
✓	1	405 ft²	405 ft²	52.3 ft	9.3 ft	1

# INPUT SUMMARY CHECKLIST REPORT

INFILTRATION													
#	Scope	Method	SLA	CFM 50	ELA	EqLA	ACH	ACH 50					
1	Wholehouse	Proposed ACH(50)	.000394	1895.3	104.05	195.68	.1876	7					

HEATING SYSTEM									
✓	#	System Type	Subtype	Efficiency	Capacity	Block	Ducts		
✓	1	Electric Heat Pump/	None	HSPF:8.5	34.6 kBtu/hr	1	sys#1		

COOLING SYSTEM									
✓	#	System Type	Subtype	Efficiency	Capacity	Air Flow	SHR	Block	Ducts
✓	1	Central Unit/	Split	SEER: 15	34.8 kBtu/hr	1044 cfm	0.75	1	sys#1

HOT WATER SYSTEM									
✓	#	System Type	SubType	Location	EF	Cap	Use	SetPnt	Conservation
✓	1	Electric	None	Garage	0.95	50 gal	60 gal	120 deg	None

SOLAR HOT WATER SYSTEM									
✓	FSEC Cert #	Company Name	System Model #	Collector Model #	Collector Area	Storage Volume	FEF		
✓	None	None			ft²				

DUCTS														
✓	#	--- Supply ---			--- Return ---		Leakage Type	Air Handler	CFM 25 TOT	CFM25 OUT	QN	RLF	HVAC #	
		Location	R-Value	Area	Location	Area							Heat	Cool
✓	1	Attic	8	361.4 ft	Attic	90.35 ft	Default Leakage	2nd Floor	(Default)	(Default)			1	1

TEMPERATURES																								
Programable Thermostat: Y						Ceiling Fans:																		
Cooling	<input type="checkbox"/>	Jan	<input type="checkbox"/>	Feb	<input type="checkbox"/>	Mar	<input type="checkbox"/>	Apr	<input type="checkbox"/>	May	<input checked="" type="checkbox"/>	Jun	<input checked="" type="checkbox"/>	Jul	<input checked="" type="checkbox"/>	Aug	<input checked="" type="checkbox"/>	Sep	<input type="checkbox"/>	Oct	<input type="checkbox"/>	Nov	<input type="checkbox"/>	Dec
Heating	<input checked="" type="checkbox"/>	Jan	<input checked="" type="checkbox"/>	Feb	<input checked="" type="checkbox"/>	Mar	<input checked="" type="checkbox"/>	Apr	<input type="checkbox"/>	May	<input type="checkbox"/>	Jun	<input type="checkbox"/>	Jul	<input type="checkbox"/>	Aug	<input type="checkbox"/>	Sep	<input type="checkbox"/>	Oct	<input checked="" type="checkbox"/>	Nov	<input checked="" type="checkbox"/>	Dec
Venting	<input type="checkbox"/>	Jan	<input type="checkbox"/>	Feb	<input checked="" type="checkbox"/>	Mar	<input checked="" type="checkbox"/>	Apr	<input type="checkbox"/>	May	<input type="checkbox"/>	Jun	<input type="checkbox"/>	Jul	<input type="checkbox"/>	Aug	<input type="checkbox"/>	Sep	<input type="checkbox"/>	Oct	<input checked="" type="checkbox"/>	Nov	<input checked="" type="checkbox"/>	Dec

# INPUT SUMMARY CHECKLIST REPORT

Thermostat Schedule: HERS 2006 Reference		Hours											
Schedule Type		1	2	3	4	5	6	7	8	9	10	11	12
Cooling (WD)	AM	78	78	78	78	78	78	78	78	80	80	80	80
	PM	80	80	78	78	78	78	78	78	78	78	78	78
Cooling (WEH)	AM	78	78	78	78	78	78	78	78	78	78	78	78
	PM	78	78	78	78	78	78	78	78	78	78	78	78
Heating (WD)	AM	66	66	66	66	66	68	68	68	68	68	68	68
	PM	68	68	68	68	68	68	68	68	68	68	66	66
Heating (WEH)	AM	66	66	66	66	66	68	68	68	68	68	68	68
	PM	68	68	68	68	68	68	68	68	68	68	66	66
MASS													
Mass Type		Area		Thickness		Furniture Fraction		Space					
Default(8 lbs/sq. ft.		0 ft²		0 ft		0.3		1st Floor					
Default(8 lbs/sq. ft.		0 ft²		0 ft		0.3		2nd Floor					

## **RESIDENTIAL ENERGY CONSERVATION CODE DOCUMENTATION CHECKLIST**

### **Florida Department of Business and Professional Regulation Simulated Performance Alternative (Performance) Method**

**Applications for compliance with the 2017 Florida Building Code, Energy Conservation via the residential Simulated Performance Method shall include:**

- ☐ *This checklist*
- ☐ *A Form R405 report that documents that the Proposed Design complies with Section R405.3 of the Florida Energy Code. This form shall include a summary page indicating home address, e-ratio and the pass or fail status along with summary areas and types of components, whether the home was simulated as a worst-case orientation, name and version of the compliance software tool, name of individual completing the compliance report (one page) and an input summary checklist that can be used for field verification (usually four pages/may be greater).*
- ☐ *Energy Performance Level (EPL) Display Card (one page)*
- ☐ *HVAC system sizing and selection based on ACCA Manual S or per exceptions provided in Section R403.7*
- ☐ *Mandatory Requirements (five pages)*

#### **Required prior to CO for the Performance Method:**

- ☐ *Air Barrier and Insulation Inspection Component Criteria checklist (Table R402.4.1.1 - one page)*
- ☐ *A completed Envelope Leakage Test Report (usually one page)*
- ☐ *If Form R405 duct leakage type indicates anything other than "default leakage", then a completed Form R405 Duct Leakage Test Report (usually one page)*

# Envelope Leakage Test Report (Blower Door Test)

## Residential Prescriptive, Performance or ERI Method Compliance 2017 Florida Building Code, Energy Conservation, 6th Edition

Jurisdiction:

Permit #:

### Job Information

Builder:

Community:

Lot: 1091

Address:

City:

State: FL

Zip:

### Air Leakage Test Results *Passing results must meet either the Performance, Prescriptive, or ERI Method*

☐ **PRESCRIPTIVE METHOD**-The building or dwelling unit shall be tested and verified as having an air leakage rate of not exceeding 7 air changes per hour at a pressure of 0.2 inch w.g. (50 Pascals) in Climate Zones 1 and 2.

☐ **PERFORMANCE or ERI METHOD**-The building or dwelling unit shall be tested and verified as having an air leakage rate of not exceeding the selected ACH(50) value, as shown on Form R405-2017 (Performance) or R406-2017 (ERI), section labeled as infiltration, sub-section ACH50.  
ACH(50) specified on Form R405-2017-Energy Calc (Performance) or R406-2017 (ERI): 7.000

$$\frac{\text{CFM}(50)}{\text{Building Volume}} \times 60 \div \frac{16245}{\text{ACH}(50)} =$$

☐ **PASS**

☐ When ACH(50) is less than 3, Mechanical Ventilation installation must be verified by building department.

Method for calculating building volume:

- ☐ Retrieved from architectural plans
- ☒ Code software calculated
- ☐ Field measured and calculated

**R402.4.1.2 Testing.** Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 Pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), *Florida Statutes*, or individuals licensed as set forth in Section 489.105(3)(f), (g), or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the *code official*. Testing shall be performed at any time after creation of all penetrations of the *building thermal envelope*.

During testing:

1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures.
2. Dampers including exhaust, intake, makeup air, back draft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures.
3. Interior doors, if installed at the time of the test, shall be open.
4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed.
5. Heating and cooling systems, if installed at the time of the test, shall be turned off.
6. Supply and return registers, if installed at the time of the test, shall be fully open.

### Testing Company

Company Name: \_\_\_\_\_ Phone: \_\_\_\_\_

I hereby verify that the above Air Leakage results are in accordance with the 2017 6th Edition Florida Building Code Energy Conservation requirements according to the compliance method selected above.

Signature of Tester: \_\_\_\_\_ Date of Test: \_\_\_\_\_

Printed Name of Tester: \_\_\_\_\_

License/Certification #: \_\_\_\_\_ Issuing Authority: \_\_\_\_\_

# ENERGY PERFORMANCE LEVEL (EPL) DISPLAY CARD

ESTIMATED ENERGY PERFORMANCE INDEX\* = 89

The lower the Energy Performance Index, the more efficient the home.

1. New home or, addition	1. <u>New (From Plans)</u>	12. Ducts, location & insulation level
2. Single-family or multiple-family	2. <u>Multi-family</u>	a) Supply ducts R <u>8.0</u>
3. No. of units (if multiple-family)	3. <u>1</u>	b) Return ducts R <u>8.0</u>
4. Number of bedrooms	4. <u>3</u>	c) AHU location <u>2nd Floor</u>
5. Is this a worst case? (yes/no)	5. <u>No</u>	13. Cooling system: Capacity <u>34.8</u>
6. Conditioned floor area (sq. ft.)	6. <u>1834</u>	a) Split system SEER <u>15.0</u>
7. Windows, type and area		b) Single package SEER <u>      </u>
a) U-factor:(weighted average)	7a. <u>0.330</u>	c) Ground/water source SEER/COP <u>      </u>
b) Solar Heat Gain Coefficient (SHGC)	7b. <u>0.230</u>	d) Room unit/PTAC EER <u>      </u>
c) Area	7c. <u>219.1</u>	e) Other <u>      </u>
8. Skylights		14. Heating system: Capacity <u>34.6</u>
a) U-factor:(weighted average)	8a. <u>NA</u>	a) Split system heat pump HSPF <u>      </u>
b) Solar Heat Gain Coefficient (SHGC)	8b. <u>NA</u>	b) Single package heat pump HSPF <u>      </u>
9. Floor type, insulation level:		c) Electric resistance COP <u>      </u>
a) Slab-on-grade (R-value)	9a. <u>0.0</u>	d) Gas furnace, natural gas AFUE <u>      </u>
b) Wood, raised (R-value)	9b. <u>13.0</u>	e) Gas furnace, LPG AFUE <u>      </u>
c) Concrete, raised (R-value)	9c. <u>      </u>	f) Other <u>8.50</u>
10. Wall type and insulation:		15. Water heating system
A. Exterior:		a) Electric resistance EF <u>0.95</u>
1. Wood frame (Insulation R-value)	10A1. <u>13.0</u>	b) Gas fired, natural gas EF <u>      </u>
2. Masonry (Insulation R-value)	10A2. <u>4.1</u>	c) Gas fired, LPG EF <u>      </u>
B. Adjacent:		d) Solar system with tank EF <u>      </u>
1. Wood frame (Insulation R-value)	10B1. <u>13.0</u>	e) Dedicated heat pump with tank EF <u>      </u>
2. Masonry (Insulation R-value)	10B2. <u>      </u>	f) Heat recovery unit HeatRec% <u>      </u>
11. Ceiling type and insulation level		g) Other <u>      </u>
a) Under attic	11a. <u>30.0</u>	16. HVAC credits claimed (Performance Method)
b) Single assembly	11b. <u>      </u>	a) Ceiling fans <u>Yes</u>
c) Knee walls/skylight walls	11c. <u>30.0</u>	b) Cross ventilation <u>No</u>
d) Radiant barrier installed	11d. <u>No</u>	c) Whole house fan <u>No</u>
		d) Multizone cooling credit <u>      </u>
		e) Multizone heating credit <u>      </u>
		f) Programmable thermostat <u>Yes</u>

\*Label required by Section R303.1.3 of the Florida Building Code, Energy Conservation, if not DEFAULT.

I certify that this home has complied with the Florida Building Code, Energy Conservation, through the above energy saving features which will be installed (or exceeded) in this home before final inspection. Otherwise, a new EPL display card will be completed based on installed code compliant features.

Builder Signature: Lillian Perrone Date: 12/6/18

Address of New Home: 4572 Arboretum CIR, Unit:BLDG 9 City/FL Zip:       , FL



## 2017 - AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA

**TABLE 402.4.1.1**  
**AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA**

Project Name: Sandbar Lot 1091 Street: City, State, Zip: , FL , Owner: Mattamy Naples LLC Design Location: FL, NAPLES_MUNICIPAL Builder Name: Permit Office: Permit Number: Jurisdiction:			CHECK
COMPONENT	AIR BARRIER CRITERIA	INSULATION INSTALLATION CRITERIA	
General requirements	A continuous air barrier shall be installed in the building envelope. The exterior thermal envelope contains a continuous air barrier. Breaks or joints in the air barrier shall be sealed.	Air-permeable insulation shall not be used as a sealing material.	
Ceiling/attic	The air barrier in any dropped ceiling/soffit shall be aligned with the insulation and any gaps in the air barrier shall be sealed. Access openings, drop down stairs or knee wall doors to unconditioned attic spaces shall be sealed.	The insulation in any dropped ceiling/soffit shall be aligned with the air barrier.	
Walls	The junction of the foundation and sill plate shall be sealed. The junction of the top plate and the top of exterior walls shall be sealed. Knee walls shall be sealed.	Cavities within corners and headers of frame walls shall be insulated by completely filling the cavity with a material having a thermal resistance of R-3 per inch minimum. Exterior thermal envelope insulation for framed walls shall be installed in substantial contact and continuous alignment with the air barrier.	
Windows, skylights and doors	The space between window/door jambs and framing, and skylights and framing shall be sealed.		
Rim joists	Rim joists shall include the air barrier.	Rim joists shall be insulated.	
Floors (including above-garage and cantilevered floors)	The air barrier shall be installed at any exposed edge of insulation.	Floor framing cavity insulation shall be installed to maintain permanent contact with the underside of subfloor decking, or floor framing cavity insulation shall be permitted to be in contact with the top side of sheathing, or continuous insulation installed on the underside of floor framing and extends from the bottom to the top of all perimeter floor framing members.	
Crawl space walls	Exposed earth in unvented crawl spaces shall be covered with a Class I vapor retarder with overlapping joints taped.	Where provided instead of floor insulation, insulation shall be permanently attached to the crawlspace	
Shafts, penetrations	Duct shafts, utility penetrations, and flue shafts opening to exterior or unconditioned space shall be sealed.		
Narrow cavities		Batts in narrow cavities shall be cut to fit, or narrow cavities shall be filled by insulation that on installation readily conforms to the available cavity spaces.	
Garage separation	Air sealing shall be provided between the garage and conditioned spaces.		
Recessed lighting	Recessed light fixtures installed in the building thermal envelope shall be sealed to the drywall.	Recessed light fixtures installed in the building thermal envelope shall be air tight and IC rated.	
Plumbing and wiring		Batt insulation shall be cut neatly to fit around wiring and plumbing in exterior walls, or insulation that on installation readily conforms to available space shall extend behind piping and wiring.	
Shower/tub on exterior wall	The air barrier installed at exterior walls adjacent to showers and tubs shall separate them from the showers and tubs.	Exterior walls adjacent to showers and tubs shall be insulated.	
Electrical/phone box on exterior walls	The air barrier shall be installed behind electrical or communication boxes or air-sealed boxes shall be installed.		
HVAC register boots	HVAC register boots that penetrate building thermal envelope shall be sealed to the sub-floor or drywall.		
Concealed sprinklers	When required to be sealed, concealed fire sprinklers shall only be sealed in a manner that is recommended by the manufacturer. Caulking or other adhesive sealants shall not be used to fill voids between fire sprinkler cover plates and walls or ceilings.		

a. In addition, inspection of log walls shall be in accordance with the provisions of ICC-400.

# Florida Building Code, Energy Conservation, 6th Edition (2017)

## Mandatory Requirements for Residential Performance, Prescriptive and ERI Methods

ADDRESS:

Permit Number:

, FL ,

**MANDATORY REQUIREMENTS** See individual code sections for full details.

### SECTION R401 GENERAL

☐ **R401.3 Energy Performance Level (EPL) display card (Mandatory).** The building official shall require that an energy performance level (EPL) display card be completed and certified by the builder to be accurate and correct before final approval of the building for occupancy. Florida law (Section 553.9085, Florida Statutes) requires the EPL display card to be included as an addendum to each sales contract for both presold and nonpresold residential buildings. The EPL display card contains information indicating the energy performance level and efficiencies of components installed in a dwelling unit. The building official shall verify that the EPL display card completed and signed by the builder accurately reflects the plans and specifications submitted to demonstrate code compliance for the building. A copy of the EPL display card can be found in Appendix RD.

☐ **R402.4 Air leakage (Mandatory).** The building thermal envelope shall be constructed to limit air leakage in accordance with the requirements of Sections R402.4.1 through R402.4.5.

**Exception:** Dwelling units of R-2 Occupancies and multiple attached single family dwellings shall be permitted to comply with Section C402.5.

☐ **R402.4.1 Building thermal envelope.** The building thermal envelope shall comply with Sections R402.4.1.1 and R402.4.1.2. The sealing methods between dissimilar materials shall allow for differential expansion and contraction.

☐ **R402.4.1.1 Installation.** The components of the building thermal envelope as listed in Table R402.4.1.1 shall be installed in accordance with the manufacturer's instructions and the criteria listed in Table R402.4.1.1, as applicable to the method of construction. Where required by the code official, an approved third party shall inspect all components and verify compliance.

☐ **R402.4.1.2 Testing.** The building or dwelling unit shall be tested and verified as having an air leakage rate not exceeding seven air changes per hour in Climate Zones 1 and 2, and three air changes per hour in Climate Zones 3 through 8. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the code official. Testing shall be performed at any time after creation of all penetrations of the building thermal envelope.

**Exception:** Testing is not required for additions, alterations, renovations, or repairs, of the building thermal envelope of existing buildings in which the new construction is less than 85 percent of the building thermal envelope.

During testing:

1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures.
2. Dampers including exhaust, intake, makeup air, backdraft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures.
3. Interior doors, if installed at the time of the test, shall be open.
4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed.
5. Heating and cooling systems, if installed at the time of the test, shall be turned off.
6. Supply and return registers, if installed at the time of the test, shall be fully open.

☐ **R402.4.2 Fireplaces.** New wood-burning fireplaces shall have tight-fitting flue dampers or doors, and outdoor combustion air. Where using tight-fitting doors on factory-built fireplaces listed and labeled in accordance with UL 127, the doors shall be tested and listed for the fireplace. Where using tight-fitting doors on masonry fireplaces, the doors shall be listed and labeled in accordance with UL 907.

☐ **R402.4.3 Fenestration air leakage.** Windows, skylights and sliding glass doors shall have an air infiltration rate of no more than 0.3 cfm per square foot (1.5 L/s/m<sup>2</sup>), and swinging doors no more than 0.5 cfm per square foot (2.6 L/s/m<sup>2</sup>), when tested according to NFRC 400 or AAMA/WDMA/CSA 101/I.S.2/A440 by an accredited, independent laboratory and listed and labeled by the manufacturer.

**Exception:** Site-built windows, skylights and doors.

## MANDATORY REQUIREMENTS - (Continued)

- ☐ **R402.4.4 Rooms containing fuel-burning appliances.** In Climate Zones 3 through 8, where open combustion air ducts provide combustion air to open combustion fuel burning appliances, the appliances and combustion air opening shall be located outside the building thermal envelope or enclosed in a room, isolated from inside the thermal envelope. Such rooms shall be sealed and insulated in accordance with the envelope requirements of Table R402.1.2, where the walls, floors and ceilings shall meet not less than the basement wall R-value requirement. The door into the room shall be fully gasketed and any water lines and ducts in the room insulated in accordance with Section R403. The combustion air duct shall be insulated where it passes through conditioned space to a minimum of R-8.

### Exceptions:

1. Direct vent appliances with both intake and exhaust pipes installed continuous to the outside.
2. Fireplaces and stoves complying with Section R402.4.2 and Section R1006 of the Florida Building Code, Residential.

- ☐ **R402.4.5 Recessed lighting.** Recessed luminaires installed in the building thermal envelope shall be sealed to limit air leakage between conditioned and unconditioned spaces. All recessed luminaires shall be IC-rated and labeled as having an air leakage rate not more than 2.0 cfm (0.944 L/s) when tested in accordance with ASTM E283 at a 1.57 psf (75 Pa) pressure differential. All recessed luminaires shall be sealed with a gasket or caulk between the housing and the interior wall or ceiling covering.

## SECTION R403 SYSTEMS

### R403.1 Controls.

- ☐ **R403.1.1 Thermostat provision (Mandatory).** At least one thermostat shall be provided for each separate heating and cooling system.

- ☐ **R403.1.3 Heat pump supplementary heat (Mandatory).** Heat pumps having supplementary electric-resistance heat shall have controls that, except during defrost, prevent supplemental heat operation when the heat pump compressor can meet the heating load.

- ☐ **R403.3.2 Sealing (Mandatory)** All ducts, air handlers, filter boxes and building cavities that form the primary air containment passageways for air distribution systems shall be considered ducts or plenum chambers, shall be constructed and sealed in accordance with Section C403.2.9.2 of the Commercial Provisions of this code and shall be shown to meet duct tightness criteria below.

Duct tightness shall be verified by testing in accordance with ANSI/RESNET/ICC 380 by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i), Florida Statutes, to be "substantially leak free" in accordance with Section R403.3.3.

- ☐ **R403.3.2.1 Sealed air handler.** Air handlers shall have a manufacturer's designation for an air leakage of no more than 2 percent of the design airflow rate when tested in accordance with ASHRAE 193.

- ☐ **R403.3.3 Duct testing (Mandatory).** Ducts shall be pressure tested to determine air leakage by one of the following methods:

1. Rough-in test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the system, including the manufacturer's air handler enclosure if installed at the time of the test. All registers shall be taped or otherwise sealed during the test.
2. Postconstruction test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the entire system, including the manufacturer's air handler enclosure. Registers shall be taped or otherwise sealed during the test.

### Exceptions:

1. A duct air leakage test shall not be required where the ducts and air handlers are located entirely within the building thermal envelope.
2. Duct testing is not mandatory for buildings complying by Section 405 of this code.

A written report of the results of the test shall be signed by the party conducting the test and provided to the code official.

- ☐ **R403.3.5 Building cavities (Mandatory).** Building framing cavities shall not be used as ducts or plenums.

- ☐ **R403.4 Mechanical system piping insulation (Mandatory).** Mechanical system piping capable of carrying fluids above 105°F (41°C) or below 55°F (13°C) shall be insulated to a minimum of R-3.

- ☐ **R403.4.1 Protection of piping insulation.** Piping insulation exposed to weather shall be protected from damage, including that caused by sunlight, moisture, equipment maintenance and wind, and shall provide shielding from solar radiation that can cause degradation of the material. Adhesive tape shall not be permitted.

- ☐ **R403.5.1 Heated water circulation and temperature maintenance systems (Mandatory)** Heated water circulation systems shall be in accordance with Section R403.5.1.1. Heat trace temperature maintenance systems shall be in accordance with Section R403.5.1.2. Automatic controls, temperature sensors and pumps shall be accessible. Manual controls shall be readily accessible.

- ☐ **R403.5.1.1 Circulation systems.** Heated water circulation systems shall be provided with a circulation pump. The system return pipe shall be a dedicated return pipe or a cold water supply pipe. Gravity and thermosiphon circulation systems shall be prohibited. Controls for circulating hot water system pumps shall start the pump based on the identification of a demand for hot water within the occupancy. The controls shall automatically turn off the pump when the water in the circulation loop is at the desired temperature and when there is no demand for hot water.

- ☐ **R403.5.1.2 Heat trace systems.** Electric heat trace systems shall comply with IEEE 515.1 or UL 515. Controls for such systems shall automatically adjust the energy input to the heat tracing to maintain the desired water temperature in the piping in accordance with the times when heated water is used in the occupancy.

## MANDATORY REQUIREMENTS - (Continued)

- ☐ **R403.5.5 Heat traps (Mandatory).** Storage water heaters not equipped with integral heat traps and having vertical pipe risers shall have heat traps installed on both the inlets and outlets. External heat traps shall consist of either a commercially available heat trap or a downward and upward bend of at least 3 ½ inches (89 mm) in the hot water distribution line and cold water line located as close as possible to the storage tank.
- R403.5.6 Water heater efficiencies (Mandatory).**
- ☐ **R403.5.6.1.1 Automatic controls.** Service water-heating systems shall be equipped with automatic temperature controls capable of adjustment from the lowest to the highest acceptable temperature settings for the intended use. The minimum temperature setting range shall be from 100°F to 140°F (38°C to 60°C).
- ☐ **R403.5.6.1.2 Shut down.** A separate switch or a clearly marked circuit breaker shall be provided to permit the power supplied to electric service systems to be turned off. A separate valve shall be provided to permit the energy supplied to the main burner(s) of combustion types of service water-heating systems to be turned off.
- ☐ **R403.5.6.2 Water-heating equipment.** Water-heating equipment installed in residential units shall meet the minimum efficiencies of Table C404.2 in Chapter 4 of the Florida Building Code, Energy Conservation, Commercial Provisions, for the type of equipment installed. Equipment used to provide heating functions as part of a combination system shall satisfy all stated requirements for the appropriate water-heating category. Solar water heaters shall meet the criteria of Section R403.5.6.2.1.
- ☐ **R403.5.6.2.1 Solar water-heating systems.** Solar systems for domestic hot water production are rated by the annual solar energy factor of the system. The solar energy factor of a system shall be determined from the Florida Solar Energy Center Directory of Certified Solar Systems. Solar collectors shall be tested in accordance with ISO Standard 9806, Test Methods for Solar Collectors, and SRCC Standard TM-1, Solar Domestic Hot Water System and Component Test Protocol. Collectors in installed solar water-heating systems should meet the following criteria:
1. Be installed with a tilt angle between 10 degrees and 40 degrees of the horizontal; and
  2. Be installed at an orientation within 45 degrees of true south.
- ☐ **R403.6 Mechanical ventilation (Mandatory).** The building shall be provided with ventilation that meets the requirements of the Florida Building Code, Residential, or Florida Building Code, Mechanical, as applicable, or with other approved means of ventilation including: Natural, Infiltration or Mechanical means. Outdoor air intakes and exhausts shall have automatic or gravity dampers that close when the ventilation system is not operating.
- ☐ **R403.6.1 Whole-house mechanical ventilation system fan efficacy.** When installed to function as a whole-house mechanical ventilation system, fans shall meet the efficacy requirements of Table R403.6.1.
- Exception:** Where whole-house mechanical ventilation fans are integral to tested and listed HVAC equipment, they shall be powered by an electronically commutated motor.
- ☐ **R403.6.2 Ventilation air.** Residential buildings designed to be operated at a positive indoor pressure or for mechanical ventilation shall meet the following criteria:
1. The design air change per hour minimums for residential buildings in ASHRAE 62.2, Ventilation for Acceptable Indoor Air Quality, shall be the maximum rates allowed for residential applications.
  2. No ventilation or air-conditioning system make-up air shall be provided to conditioned space from attics, crawlspaces, attached enclosed garages or outdoor spaces adjacent to swimming pools or spas.
  3. If ventilation air is drawn from enclosed space(s), then the walls of the space(s) from which air is drawn shall be insulated to a minimum of R-11 and the ceiling shall be insulated to a minimum of R-19, space permitting, or R-10 otherwise.
- R403.7 Heating and cooling equipment (Mandatory).**
- ☐ **R403.7.1 Equipment sizing.** Heating and cooling equipment shall be sized in accordance with ACCA Manual S based on the equipment loads calculated in accordance with ACCA Manual J or other approved heating and cooling calculation methodologies, based on building loads for the directional orientation of the building. The manufacturer and model number of the outdoor and indoor units (if split system) shall be submitted along with the sensible and total cooling capacities at the design conditions described in Section R302.1. This Code does not allow designer safety factors, provisions for future expansion or other factors that affect equipment sizing. System sizing calculations shall not include loads created by local intermittent mechanical ventilation such as standard kitchen and bathroom exhaust systems. New or replacement heating and cooling equipment shall have an efficiency rating equal to or greater than the minimum required by federal law for the geographic location where the equipment is installed.

**TABLE R403.6.1  
WHOLE-HOUSE MECHANICAL VENTILATION SYSTEM FAN EFFICACY**

FAN LOCATION	AIRFLOW RATE MINIMUM (CFM)	MINIMUM EFFICACY <sup>a</sup> (CFM/WATT)	AIRFLOW RATE MAXIMUM (CFM)
Range hoods	Any	2.8 cfm/watt	Any
In-line fan	Any	2.8 cfm/watt	Any
Bathroom, utility room	10	1.4 cfm/watt	<90
Bathroom, utility room	90	2.8 cfm/watt	Any

For SI: 1 cfm = 28.3 L/min.

a. When tested in accordance with HVI Standard 916

## MANDATORY REQUIREMENTS - (Continued)

- ☐ **R403.7.1.1 Cooling equipment capacity.** Cooling only equipment shall be selected so that its total capacity is not less than the calculated total load but not more than 1.15 times greater than the total load calculated according to the procedure selected in Section 403.7, or the closest available size provided by the manufacturer's product lines. The corresponding latent capacity of the equipment shall not be less than the calculated latent load.

The published value for AHRI total capacity is a nominal, rating-test value and shall not be used for equipment sizing. Manufacturer's expanded performance data shall be used to select cooling-only equipment. This selection shall be based on the outdoor design dry-bulb temperature for the load calculation (or entering water temperature for water-source equipment), the blower CFM provided by the expanded performance data, the design value for entering wet-bulb temperature and the design value for entering dry-bulb temperature.

Design values for entering wet-bulb and dry-bulb temperatures shall be for the indoor dry bulb and relative humidity used for the load calculation and shall be adjusted for return side gains if the return duct(s) is installed in an unconditioned space.

Exceptions:

1. Attached single- and multiple-family residential equipment sizing may be selected so that its cooling capacity is less than the calculated total sensible load but not less than 80 percent of that load.
2. When signed and sealed by a Florida-registered engineer, in attached single- and multiple-family units, the capacity of equipment may be sized in accordance with good design practice.

### R403.7.1.2 Heating equipment capacity.

- ☐ **R403.7.1.2.1 Heat pumps.** Heat pump sizing shall be based on the cooling requirements as calculated according to Section R403.7.1.1, and the heat pump total cooling capacity shall not be more than 1.15 times greater than the design cooling load even if the design heating load is 1.15 times greater than the design cooling load.

- ☐ **R403.7.1.2.2 Electric resistance furnaces.** Electric resistance furnaces shall be sized within 4 kW of the design requirements calculated according to the procedure selected in Section R403.7.1.

- ☐ **R403.7.1.2.3 Fossil fuel heating equipment.** The capacity of fossil fuel heating equipment with natural draft atmospheric burners shall not be less than the design load calculated in accordance with Section R403.7.1.

- ☐ **R403.7.1.3 Extra capacity required for special occasions.** Residences requiring excess cooling or heating equipment capacity on an intermittent basis, such as anticipated additional loads caused by major entertainment events, shall have equipment sized or controlled to prevent continuous space cooling or heating within that space by one or more of the following options:

1. A separate cooling or heating system is utilized to provide cooling or heating to the major entertainment areas.
2. A variable capacity system sized for optimum performance during base load periods is utilized.

- ☐ **R403.8 Systems serving multiple dwelling units (Mandatory).** Systems serving multiple dwelling units shall comply with Sections C403 and C404 of the IECC—Commercial Provisions in lieu of Section R403.

- ☐ **R403.9 Snow melt and ice system controls (Mandatory)** Snow- and ice-melting systems, supplied through energy service to the building, shall include automatic controls capable of shutting off the system when the pavement temperature is above 50°F (10°C), and no precipitation is falling and an automatic or manual control that will allow shutoff when the outdoor temperature is above 40°F (4.8°C).

- ☐ **R403.10 Pools and permanent spa energy consumption (Mandatory).** The energy consumption of pools and permanent spas shall be in accordance with Sections R403.10.1 through R403.10.5.

- ☐ **R403.10.1 Heaters.** The electric power to heaters shall be controlled by a readily accessible on-off switch that is an integral part of the heater mounted on the exterior of the heater, or external to and within 3 feet (914 mm) of the heater. Operation of such switch shall not change the setting of the heater thermostat. Such switches shall be in addition to a circuit breaker for the power to the heater. Gas-fired heaters shall not be equipped with continuously burning ignition pilots.

- ☐ **R403.10.2 Time switches.** Time switches or other control methods that can automatically turn off and on according to a preset schedule shall be installed for heaters and pump motors. Heaters and pump motors that have built-in time switches shall be in compliance with this section.

Exceptions:

1. Where public health standards require 24-hour pump operation.
2. Pumps that operate solar- and waste-heat-recovery pool heating systems.
3. Where pumps are powered exclusively from on-site renewable generation.

- ☐ **R403.10.3 Covers.** Outdoor heated swimming pools and outdoor permanent spas shall be equipped with a vapor-retardant cover on or at the water surface or a liquid cover or other means proven to reduce heat loss.

**Exception:** Where more than 70 percent of the energy for heating, computed over an operation season, is from site-recovered energy, such as from a heat pump or solar energy source, covers or other vapor-retardant means shall not be required.

- ☐ **R403.10.4 Gas- and oil-fired pool and spa heaters.** All gas- and oil-fired pool and spa heaters shall have a minimum thermal efficiency of 82 percent for heaters manufactured on or after April 16, 2013, when tested in accordance with ANSI Z 21.56. Pool heaters fired by natural or LP gas shall not have continuously burning pilot lights.

- ☐ **R403.10.5 Heat pump pool heaters.** Heat pump pool heaters shall have a minimum COP of 4.0 when tested in accordance with AHRI 1160, Table 2, Standard Rating Conditions-Low Air Temperature. A test report from an independent laboratory is required to verify procedure compliance. Geothermal swimming pool heat pumps are not required to meet this standard.
- ☐ **R403.11 Portable spas (Mandatory)** The energy consumption of electric-powered portable spas shall be controlled by the requirements of APSP-14.

## SECTION R404

### ELECTRICAL POWER AND LIGHTING SYSTEMS

- ☐ **R404.1 Lighting equipment (Mandatory).** Not less than 75 percent of the lamps in permanently installed lighting fixtures shall be high-efficacy lamps or not less than 75 percent of the permanently installed lighting fixtures shall contain only high-efficacy lamps.
- Exception:** Low-voltage lighting.
- R404.1.1 Lighting equipment (Mandatory)** Fuel gas lighting systems shall not have continuously burning pilot lights.

# System Sizing Calculations - Summer

## Residential Load - Whole House Component Details

Mattamy Naples LLC

Project Title:  
Sandbar Lot 1091

, FL

12/5/2018

Reference City: Naples, FL

Temperature Difference: 16.0F(TMY3 99%) Humidity difference: 58gr.

### Component Loads for Whole House

Window	Type*						Overhang		Window Area(sqft)			HTM		Load	
	Panes	SHGC	U	InSh	IS	Ornt	Len	Hgt	Gross	Shaded	Unshaded	Shaded	Unshaded		
1	2 NFRC	0.23, 0.33	No	No	S		11.6f	0.2ft.	48.0	48.0	0.0	10	11	492	Btuh
2	2 NFRC	0.23, 0.33	No	No	W		1.0ft.	0.4ft.	30.0	2.5	27.5	10	28	787	Btuh
3	2 NFRC	0.23, 0.33	No	No	W		1.0ft.	1.7ft.	20.0	0.0	20.0	10	28	554	Btuh
4	2 NFRC	0.23, 0.33	No	No	W		7.3ft.	0.0ft.	21.3	21.3	0.0	10	28	218	Btuh
5	2 NFRC	0.23, 0.33	No	No	W		7.3ft.	0.0ft.	11.8	11.8	0.0	10	28	121	Btuh
6	2 NFRC	0.23, 0.33	No	No	E		1.3ft.	0.8ft.	40.0	2.9	37.1	10	28	1058	Btuh
7	2 NFRC	0.23, 0.33	No	No	E		16.0f	0.2ft.	48.0	48.0	0.0	10	28	492	Btuh
	Excursion													652	Btuh
	Window Total								219 (sqft)					4374 Btuh	
Walls	Type						U-Value	R-Value	Area(sqft)			HTM		Load	
								Cav/Sheath							
1	Frame - Wood - Ext						0.09	13.0/0.0	76.0			2.0		152	Btuh
2	Concrete Blk,Hollow - Ext						0.15	4.1/0.0	31.3			1.8		56	Btuh
3	Frame - Wood - Ext						0.09	13.0/0.0	130.0			2.0		260	Btuh
4	Concrete Blk,Hollow - Ext						0.15	4.1/0.0	69.6			1.8		125	Btuh
5	Frame - Wood - Ext						0.09	13.0/0.0	32.0			2.0		64	Btuh
6	Concrete Blk,Hollow - Ext						0.15	4.1/0.0	84.7			1.8		152	Btuh
7	Frame - Wood - Adj						0.09	13.0/0.0	251.0			1.4		356	Btuh
9	Concrete Blk,Hollow - Ext						0.15	4.1/0.0	466.7			1.8		836	Btuh
10	Concrete Blk,Hollow - Ext						0.15	4.1/0.0	400.0			1.8		716	Btuh
11	Concrete Blk,Hollow - Ext						0.15	4.1/0.0	112.0			1.8		201	Btuh
	Wall Total								1653 (sqft)					2917 Btuh	
Doors	Type						Area (sqft)			HTM		Load			
1	- Garage						17.8			0.0		0 Btuh			
	Door Total						18 (sqft)					0 Btuh			
Ceilings	Type/Color/Surface						U-Value	R-Value	Area(sqft)			HTM		Load	
1	Knee Wall/Light/Tile						0.032	30.0/0.0	160.0			0.83		132	Btuh
2	Knee Wall/Light/Tile						0.032	30.0/0.0	40.0			0.83		33	Btuh
3	Vented Attic/Light/Tile						0.032	30.0/0.0	753.0			0.83		624	Btuh
4	Vented Attic/Light/Tile						0.032	30.0/0.0	614.0			0.83		508	Btuh
	Ceiling Total								1567 (sqft)					1298 Btuh	
Floors	Type						R-Value		Size			HTM		Load	
1	Raised Wood - Adj						13.0		184 (sqft)			0.7		135	Btuh
2	Slab On Grade						0.0		1210 (ft-perimeter)			0.0		0	Btuh
3	Interior						0.0		440 (sqft)			0.0		0	Btuh
	Floor Total								1834.0 (sqft)					135 Btuh	
	Envelope Subtotal:													8723 Btuh	

# Manual J Summer Calculations

## Residential Load - Component Details (continued)

Mattamy Naples LLC

Project Title:  
Sandbar Lot 1091

Climate:FL\_NAPLES\_MUNICIPAL

, FL

12/5/2018

<b>Infiltration</b>	Type Natural	Average ACH 0.23	Volume(cuft) 16245	Wall Ratio 1	CFM= 61.0	Load 1073 Btuh
<b>Internal gain</b>		Occupants 4	Btuh/occupant X 230	Appliance +	5200	Load 6120 Btuh
					Sensible Envelope Load:	15916 Btuh
<b>Duct load</b>	Average sealed, Supply(R8.0-Attic), Return(R8.0-Attic)				(DGM of 0.177)	2825 Btuh
					<b>Sensible Load All Zones</b>	<b>18741 Btuh</b>



# Manual J Summer Calculations

## Residential Load - Component Details (continued)

Mattamy Naples LLC

Project Title:  
Sandbar Lot 1091

Climate:FL\_NAPLES\_MUNICIPAL

, FL

12/5/2018

### WHOLE HOUSE TOTALS

<b>Whole House Totals for Cooling</b>	<b>Sensible Envelope Load All Zones</b>	<b>15916 Btuh</b>
	Sensible Duct Load	2825 Btuh
	<b>Total Sensible Zone Loads</b>	<b>18741 Btuh</b>
	Sensible ventilation	0 Btuh
	Blower	0 Btuh
	<b>Total sensible gain</b>	<b>18741 Btuh</b>
	Latent infiltration gain (for 58 gr. humidity difference)	2404 Btuh
	Latent ventilation gain	0 Btuh
	Latent duct gain	1136 Btuh
	Latent occupant gain (4.0 people @ 200 Btuh per person)	800 Btuh
	Latent other gain	0 Btuh
	<b>Latent total gain</b>	<b>4340 Btuh</b>
	<b>TOTAL GAIN</b>	<b>23080 Btuh</b>

### EQUIPMENT

1. Central Unit	Carrier #25HBC536A**30	34800 Btuh
-----------------	------------------------	------------

\*Key: Window types (Panels - Number and type of panes of glass)  
 (SHGC - Shading coefficient of glass as SHGC numerical value)  
 (U - Window U-Factor)  
 (InSh - Interior shading device: none(No), Blinds(B), Draperies(D) or Roller Shades(R))  
     - For Blinds: Assume medium color, half closed  
     For Draperies: Assume medium weave, half closed  
     For Roller shades: Assume translucent, half closed  
 (IS - Insect screen: none(N), Full(F) or Half(½))  
 (Ornt - compass orientation)



Version 8

# System Sizing Calculations - Winter

## Residential Load - Whole House Component Details

Mattamy Naples LLC

Project Title:  
Sandbar Lot 1091  
Building Type: User

, FL

12/5/2018

Reference City: Naples, FL (Defaults) Winter Temperature Difference: 27.0 F (TMY3 99%)

### Component Loads for Whole House

Window	Panes/Type	Frame	U	Orientation	Area(sqft)	X	HTM=	Load
1	2, NFRC 0.23	Vinyl	0.33	S	48.0		8.9	428 Btuh
2	2, NFRC 0.23	Vinyl	0.33	W	30.0		8.9	267 Btuh
3	2, NFRC 0.23	Vinyl	0.33	W	20.0		8.9	178 Btuh
4	2, NFRC 0.23	Vinyl	0.33	W	21.3		8.9	189 Btuh
5	2, NFRC 0.23	Vinyl	0.33	W	11.8		8.9	105 Btuh
6	2, NFRC 0.23	Vinyl	0.33	E	40.0		8.9	356 Btuh
7	2, NFRC 0.23	Vinyl	0.33	E	48.0		8.9	428 Btuh
	Window Total				219.1(sqft)			1952 Btuh
Walls	Type	Ornt.	Ueff.	R-Value (Cav/Sh)	Area	X	HTM=	Load
1	Frame - Wood	- Ext	(0.089)	13.0/0.0	76		2.40	182 Btuh
2	Conc Blk,Hollow	- Ext	(0.149)	4.1/0.0	31		4.03	126 Btuh
3	Frame - Wood	- Ext	(0.089)	13.0/0.0	130		2.40	312 Btuh
4	Conc Blk,Hollow	- Ext	(0.149)	4.1/0.0	70		4.03	280 Btuh
5	Frame - Wood	- Ext	(0.089)	13.0/0.0	32		2.40	77 Btuh
6	Conc Blk,Hollow	- Ext	(0.149)	4.1/0.0	85		4.03	341 Btuh
7	Frame - Wood	- Adj	(0.089)	13.0/0.0	251		2.40	601 Btuh
9	Conc Blk,Hollow	- Ext	(0.149)	4.1/0.0	467		4.03	1880 Btuh
10	Conc Blk,Hollow	- Ext	(0.149)	4.1/0.0	400		4.03	1612 Btuh
11	Conc Blk,Hollow	- Ext	(0.149)	4.1/0.0	112		4.03	451 Btuh
	Wall Total				1653(sqft)			5863 Btuh
Doors	Type	Storm	Ueff.		Area	X	HTM=	Load
1	- Garage,	n	(0.000)		18		0.0	0 Btuh
	Door Total				18(sqft)			0Btuh
Ceilings	Type/Color/Surface	Ueff.	R-Value		Area	X	HTM=	Load
1	Knee Wall/L/Tile	(0.032)	30.0/0.0		160		0.9	138 Btuh
2	Knee Wall/L/Tile	(0.032)	30.0/0.0		40		0.9	34 Btuh
3	Vented Attic/L/Tile	(0.032)	30.0/0.0		753		0.9	647 Btuh
4	Vented Attic/L/Tile	(0.032)	30.0/0.0		614		0.9	528 Btuh
	Ceiling Total				1567(sqft)			1347Btuh
Floors	Type	Ueff.	R-Value		Size	X	HTM=	Load
1	Raised Wood - Adj	(0.067)	13.0		184.0 sqft		1.8	331 Btuh
2	Slab On Grade	(1.180)	0.0		50.0 ft(perim.)		31.9	1593 Btuh
3	Interior	(1.180)	0.0		440.0 sqft		0.0	0 Btuh
	Floor Total				1834 sqft			1924 Btuh
	Envelope Subtotal:							11086 Btuh
Infiltration	Type	Wholehouse	ACH	Volume(cuft)	Wall Ratio	CFM=		
	Natural		0.30	16245	1.00	81.3		2414 Btuh

# Manual J Winter Calculations

## Residential Load - Component Details (continued)

Mattamy Naples LLC

Project Title:  
Sandbar Lot 1091  
Building Type: User

, FL

12/5/2018

<b>Duct load</b>	Average sealed, R8.0, Supply(Att), Return(Att) (DLM of 0.221)	2984 Btuh
<b>All Zones</b>	<b>Sensible Subtotal All Zones</b>	<b>16484 Btuh</b>

### WHOLE HOUSE TOTALS

<b>Totals for Heating</b>	Subtotal Sensible Heat Loss Ventilation Sensible Heat Loss Total Heat Loss	16484 Btuh 0 Btuh 16484 Btuh
---------------------------	--	------------------------------------

### EQUIPMENT

1. Electric Heat Pump	Carrier #25HBC536A**30	34600 Btuh
-----------------------	------------------------	------------

Key: Window types - NFRC (Requires U-Factor and Shading coefficient(SHGC) of glass as numerical values)  
or - Glass as 'Clear' or 'Tint' (Uses U-Factor and SHGC defaults)  
U - (Window U-Factor)  
HTM - (ManualJ Heat Transfer Multiplier)



Version 8

# Residential System Sizing Calculation

## Summary

Mattamy Naples LLC

Project Title:  
Sandbar Lot 1091

, FL


12/5/2018

Location for weather data: Naples, FL - Defaults: Latitude(26.15) Altitude(3 ft.) Temp Range(M)			
Humidity data: Interior RH (50%) Outdoor wet bulb (78F) Humidity difference(58gr.)			
Winter design temperature(TMY3 99%)	43 F	Summer design temperature(TMY3 99%)	91 F
Winter setpoint	70 F	Summer setpoint	75 F
Winter temperature difference	27 F	Summer temperature difference	16 F
<b>Total heating load calculation</b>	<b>16484 Btuh</b>	<b>Total cooling load calculation</b>	<b>23080 Btuh</b>
Submitted heating capacity	% of calc Btuh	Submitted cooling capacity	% of calc Btuh
Total (Electric Heat Pump)	209.9 34600	Sensible (SHR = 0.75)	139.3 26100
Heat Pump + Auxiliary(0.0kW)	209.9 34600	Latent	200.5 8700
		<b>Total (Electric Heat Pump)</b>	<b>150.8 34800</b>

## WINTER CALCULATIONS

Winter Heating Load (for 1834 sqft)


Load component	Load
Window total 219 sqft	1952 Btuh
Wall total 1653 sqft	5863 Btuh
Door total 18 sqft	0 Btuh
Ceiling total 1567 sqft	1347 Btuh
Floor total See detail report	1924 Btuh
Infiltration 81 cfm	2414 Btuh
Duct loss	2984 Btuh
<b>Subtotal</b>	<b>16484 Btuh</b>
Ventilation 0 cfm	0 Btuh
<b>TOTAL HEAT LOSS</b>	<b>16484 Btuh</b>

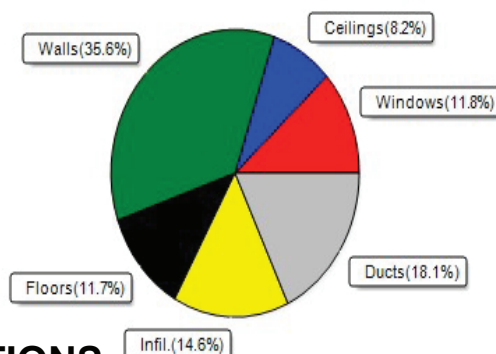

## SUMMER CALCULATIONS

Summer Cooling Load (for 1834 sqft)

Load component	Load
Window total 219 sqft	4374 Btuh
Wall total 1653 sqft	2917 Btuh
Door total 18 sqft	0 Btuh
Ceiling total 1567 sqft	1298 Btuh
Floor total	135 Btuh
Infiltration 61 cfm	1073 Btuh
Internal gain	6120 Btuh
Duct gain	2825 Btuh
Sens. Ventilation 0 cfm	0 Btuh
Blower Load	0 Btuh
<b>Total sensible gain</b>	<b>18741 Btuh</b>
Latent gain(ducts)	1136 Btuh
Latent gain(infiltration)	2404 Btuh
Latent gain(ventilation)	0 Btuh
Latent gain(internal/occupants/other)	800 Btuh
<b>Total latent gain</b>	<b>4340 Btuh</b>
<b>TOTAL HEAT GAIN</b>	<b>23080 Btuh</b>

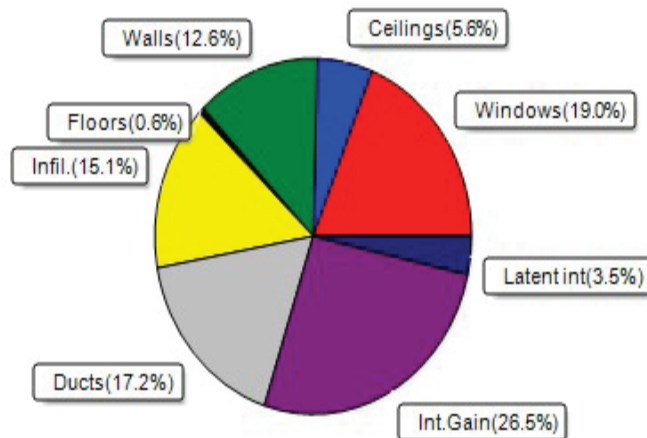

8th Edition

EnergyGauge® / USRCZB v6.1

Digitally signed by David A  
DaSilva  
DN: c=US, o=IdenTrust ACES  
PREPARED BY: Unaffiliated Individual, cn=David  
DATE: A DaSilva,  
0.9.2342.19200300.100.1.1=A010  
98000000163892A5AE700001488  
Date: 2018.12.05 17:10:33 -05'00'
